


August 16, 2024

Project Status Overview

The Works Phase LED Conversion of City-owned streetlights continued installation since last report. In total, 332 luminaires have been installed, which is 67% of the project scope.

Looking ahead, Dalkia will finish up work on the decorative lights along Main St and Reinken Ave, and then the NMDOT lights along the I-25 Bypass.

The map below shows progress between June 10, 2024 and August 16, 2024.

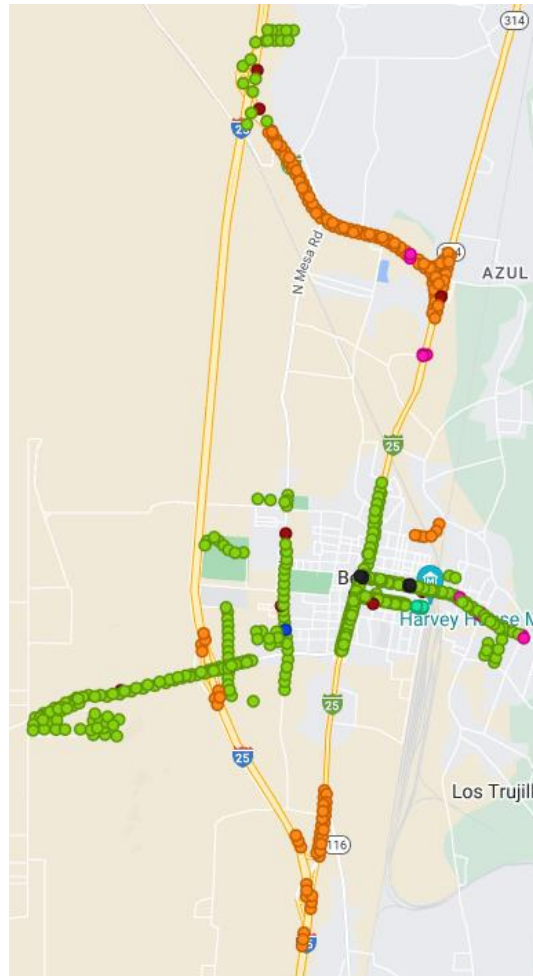

LEGEND

LIGHT GREEN: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade
