


September 6, 2024

Project Status Overview

The Works Phase LED Conversion of City-owned streetlights continued installation since last report. In total, 426 luminaires have been installed, which is 85% of the project scope.

To complete the remainder of the scope, Dalkia will perform installation on the traffic signal lights along Main St and Reinken Ave and the NMDOT lights along the I-25 Bypass and I-25 on/off ramps.

The map below shows progress between June 10, 2024 and September 6, 2024.

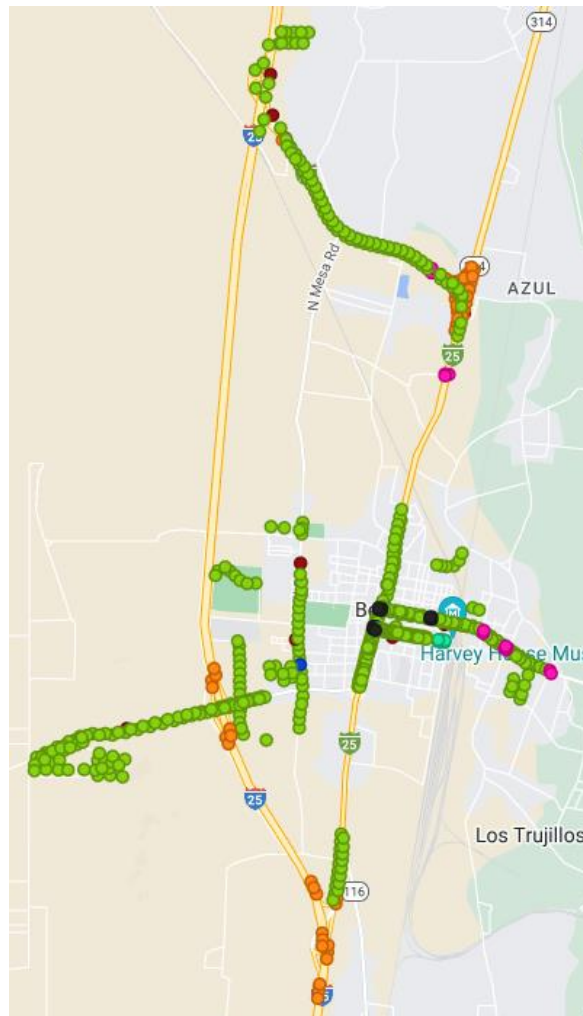

LEGEND

LIGHT GREEN: Upgrade Complete
ALL OTHER COLORS: Scheduled for Upgrade
